




## CM Formal Projects Construction Schedules

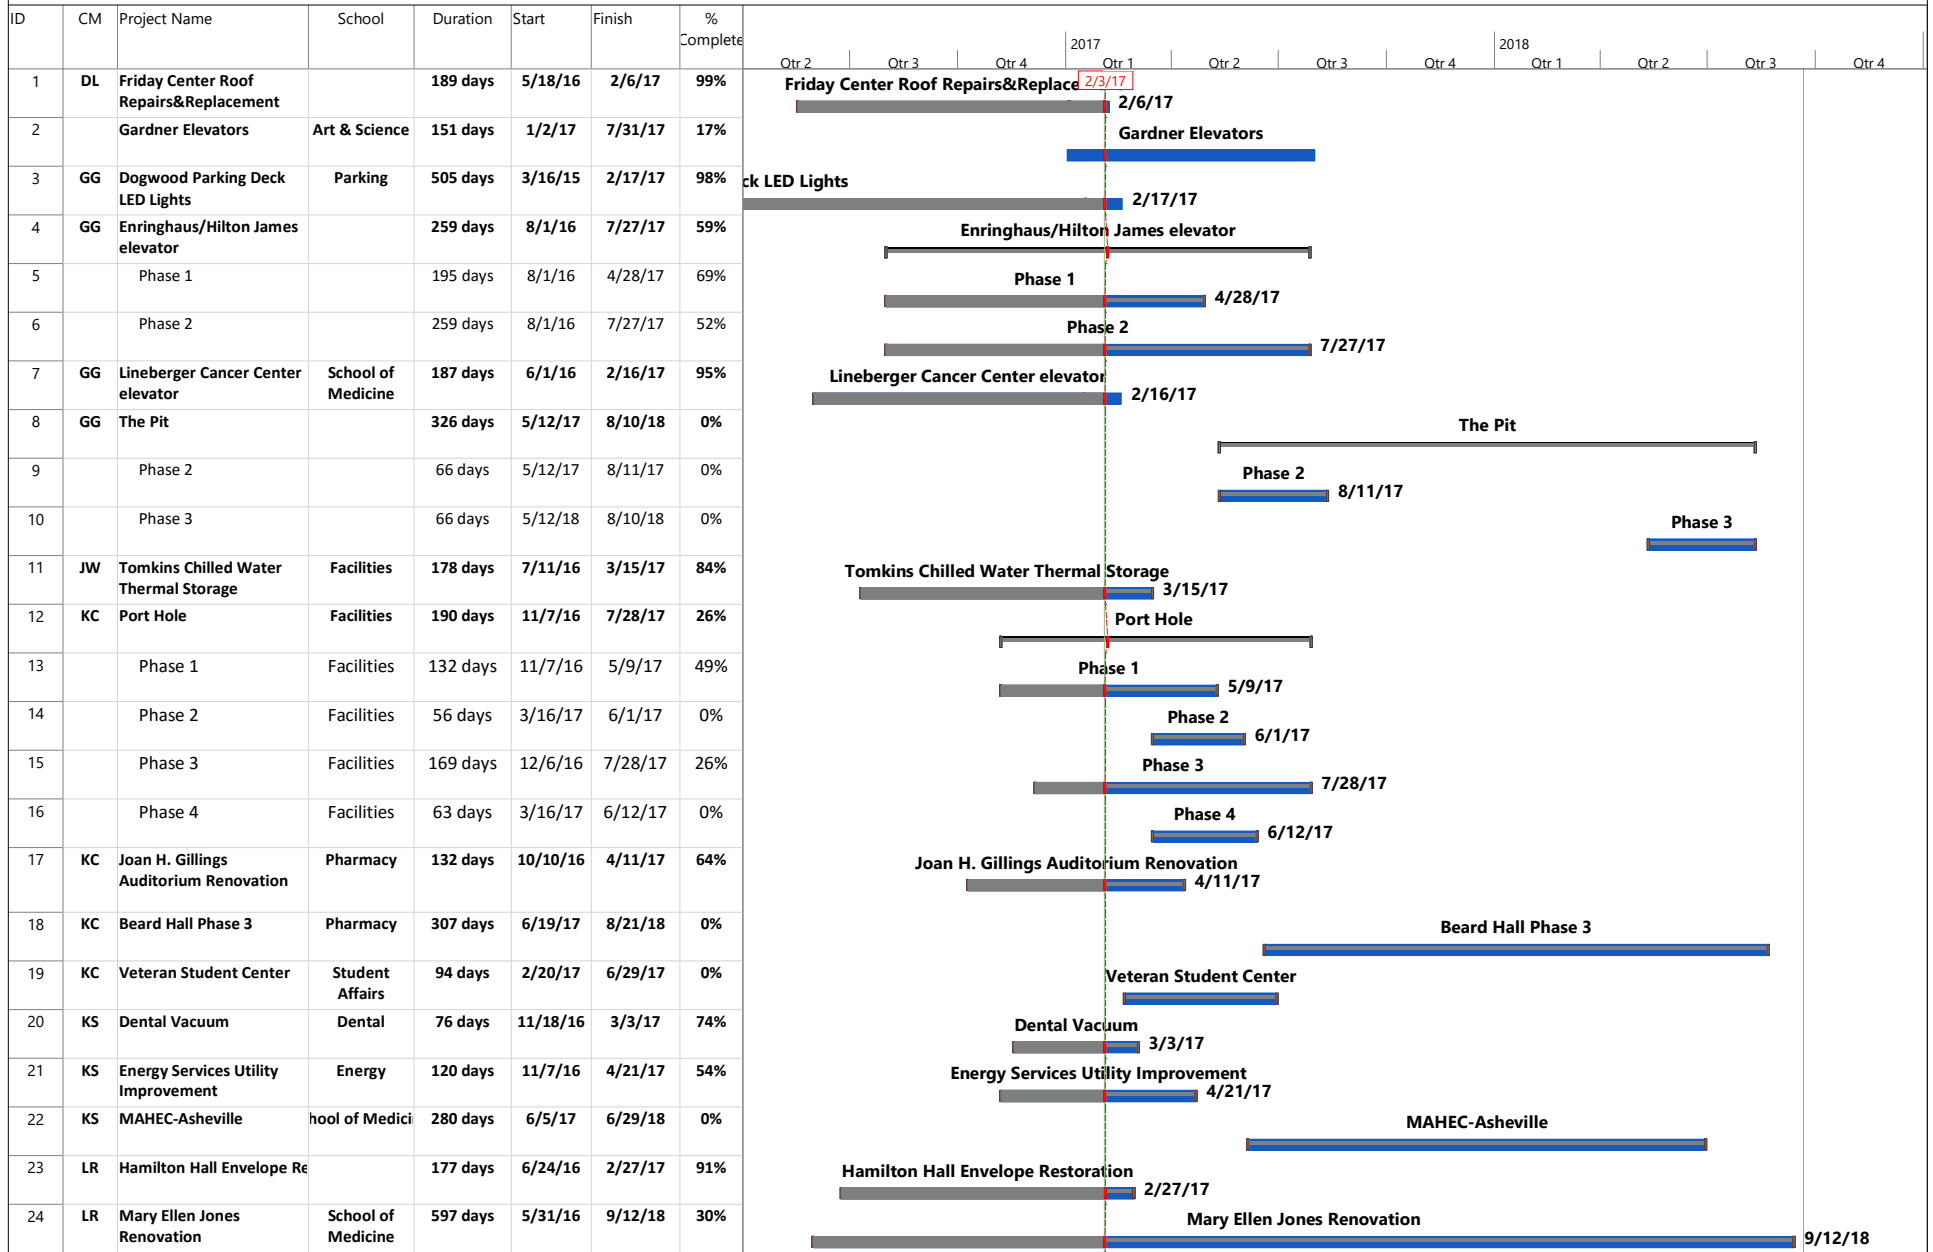

Project: Formal Project 1-31-17  
Date: 2/3/17

Task Summary Manual Task Deadline Baseline Milestone Progress   
 Milestone Project Summary Manual Summary Baseline Baseline Summary



## CM Formal Projects Construction Schedules

ID	CM	Project Name	School	Duration	Start	Finish	% Complete	Timeline (Qtr 2, Qtr 3, Qtr 4 2017, Qtr 1, Qtr 2, Qtr 3, Qtr 4 2018)											
25	LR	Kenan Lab Renov. 8-9th floor & HVAC Upgrade	Art & Science	262 days	5/22/17	5/22/18	0%												
26		<b>Non-Traditional Projects</b>		504 days	10/17/16	9/20/18	9%												
27	KC	Barnes & Noble Book Store	Enterprise	80 days	3/13/17	6/30/17	0%												
28	KS	Indoor Practice Facility	Athletics'	404 days	3/6/17	9/20/18	0%												
29	KS	Fetzer stadium (Lax/Soccer)	Athletics'	404 days	3/6/17	9/20/18	0%												
30	KS	Henry Stadium	Athletics	404 days	3/6/17	9/20/18	0%												
31	KS	Van Heck-Wettach Asbestos	Law School	196 days	12/1/16	8/31/17	25%												
32		Phase 2B-Lobby Phase		27 days	12/1/16	1/6/17	100%												
33		Phase 3		80 days	5/12/17	8/31/17	0%												
34	DL	Boshamer Baseball visitor locker room	Athletic	140 days	10/17/16	4/28/17	57%												
35	DL	Finley Fields-South	Athletic	67 days	11/15/16	2/15/17	88%												
36	DL	Finley Fields-North	Athletic	212 days	3/1/17	12/21/17	0%												
37	DL	Kenan Field Renovation	Athletic	84 days	4/3/17	7/27/17	0%												

Project: Formal Project 1-31-17  
Date: 2/3/17

Task Summary Manual Task Deadline Baseline Milestone Progress   
 Milestone Project Summary Manual Summary Baseline Baseline Summary
